

working for clean rivers

Marx & 105th Pump Station-Amend PTE Contract (E11044)

Lisa Moscinski | Project Manager | Bureau of Environmental Services

March 20, 2024



ENVIRONMENTAL SERVICES
CITY OF PORTLAND

Mingus Mapps, Commissioner
Dawn Uchiyama, Director



Project Requirements

- Amend Contract with Consor North America, Inc.
- Additional design engineering services are required to update and design the pump station at a new site.



NE. 105TH AVE & NE. MARX ST.
5550 NE 105TH




Project Objectives

- Replace existing pump station to improve reliability and maintenance.



Project Overview

- Original scope of the contract was to rebuild and expand by acquiring an easement on adjacent property.
- Determined easement would have negative impacts to business on adjacent property.
- Relocate the pump station across the street at a property BES is in the process of purchasing, Pursuant to Ordinance No. 191509.

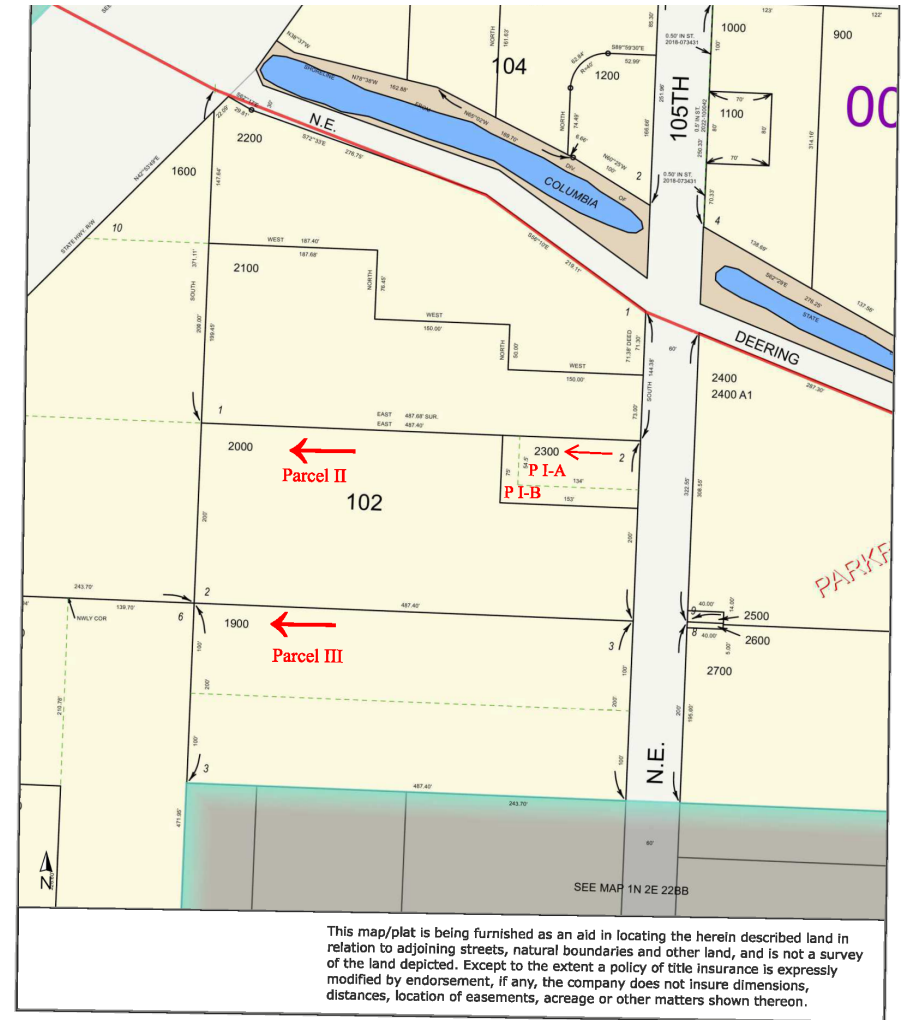

Project Overview

Scope of Services:

1. Update a portion of the Pre-Design Task for the new pump station location at 5635 NE 105th Ave.
2. Update Design for the new pump station location at 5635 NE 105th Ave.
3. Design sewer realignment to divert flows to new pump station location at 5635 NE 105th Ave and force main extension to connect to the existing force main at the current pump station location.



Project Budget and Schedule

- Extend term from March 1, 2025 to **June 30, 2027.**
- Increase contract not-to-exceed amount of \$909,648 by \$458,676 to a new total not-to-exceed amount of **\$1,368,324.**



Questions

Thank you

