RegJIN

Portland City Council Presentation

June 12, 2013

Christine Moody
Chief Procurement Officer

Chief Mike Reese
Portland Police Bureau

Agenda

1. CPO Christine Moody - Project History

2. Chief Mike Reese – Why Now

3. Capt. John Brooks – Budget, Selection Process, Timeline

4. CTO Ben Berry - Technology Accountability

5. Jeff Baer - Contract Safeguards

6. Q and A

Why Now?

PPDS is Old (1982 – Same year as the Commodore 64)
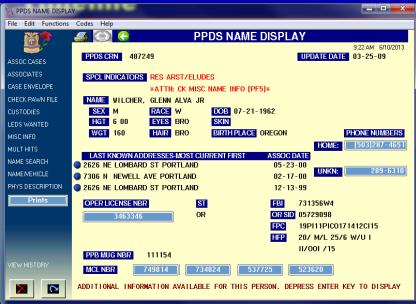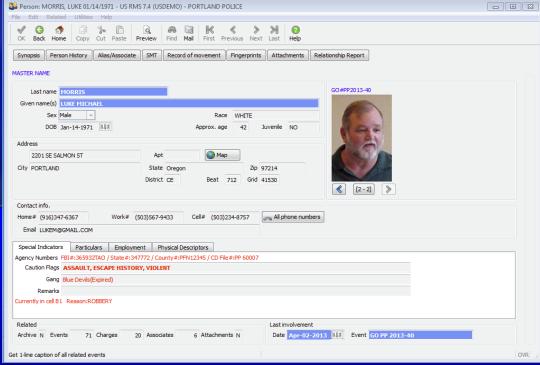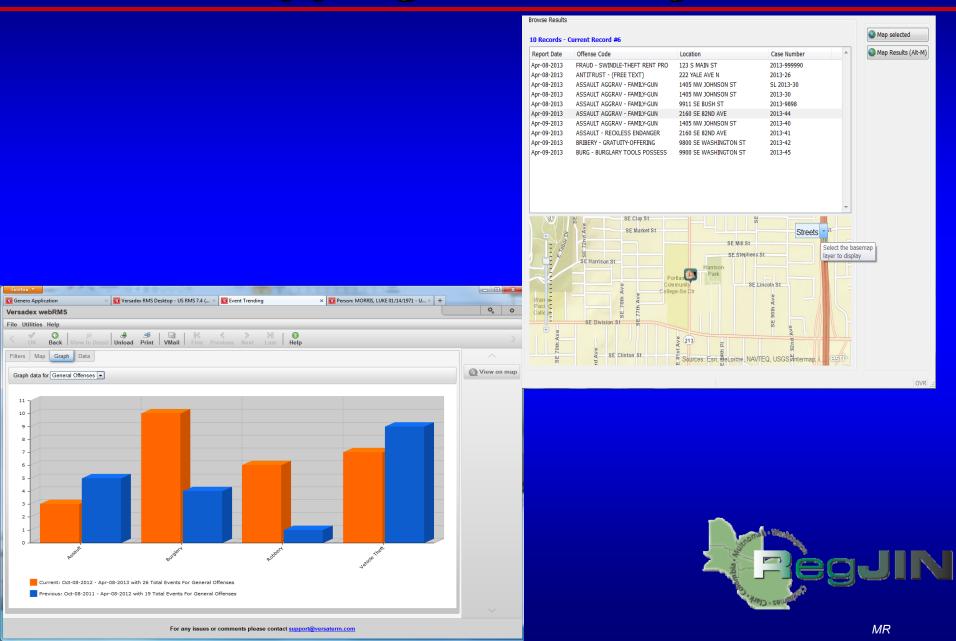
No longer supported

RegJIN Does More

Crime Mapping and Analysis

MR

Partners

Banks	Hillsboro	Scappoose
Battle Ground	King City	Sherwood
Beaverton	La Center	St. Helens
Camas	Lake Oswego	Tigard
Canby	Milwaukie	Troutdale
Clark County	Multnomah County	Tualatin
Clatskanie	North Plains	Vancouver
Columbia County	OHSU Public Safety	Vernonia
Cornelius	Portland Police	Washington County
Fairview	Port of Portland	WSU Public Safety
Forest Grove	Police	Washougal
Gaston	PSU Public Safety	
Gladstone	Rainer	
Gresham	Ridgefield	

MR
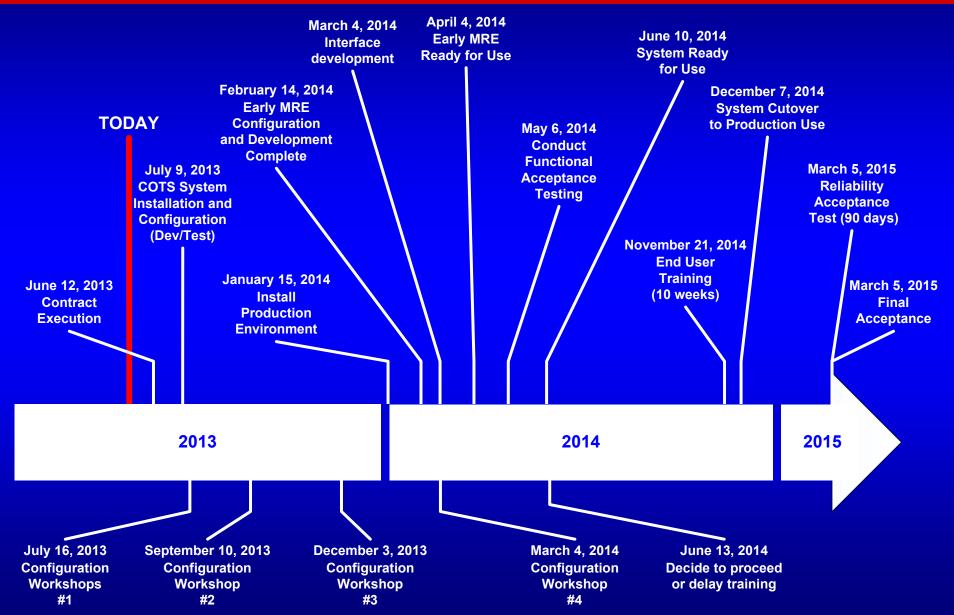
Why Now?

1. PPDS is Old (1982 –No longer supported)

2. RegJIN has more features

3. Timely Data Entry

4. More partners means a more robust system

5. Increased benefit to the community

MR

Project Schedule

TODAY

June 12, 2013
Contract
Execution

July 9, 2013
COTS System
Installation and
Configuration
(Dev/Test)

February 14, 2014
Early MRE
Configuration
and Development
Complete

January 15, 2014
Install
Production
Environment

March 4, 2014
Interface
development

April 4, 2014
Early MRE
Ready for Use

May 6, 2014
Conduct
Functional
Acceptance
Testing

June 10, 2014
System Ready
for Use

December 7, 2014
System Cutover
to Production Use

November 21, 2014
End User
Training
(10 weeks)

March 5, 2015
Reliability
Acceptance
Test (90 days)

March 5, 2015
Final
Acceptance

2013

2014

2015

July 16, 2013
Configuration
Workshops
#1

September 10, 2013
Configuration
Workshop
#2

December 3, 2013
Configuration
Workshop
#3

March 4, 2014
Configuration
Workshop
#4

June 13, 2014
Decide to proceed
or delay training

JB

Questions?
